

EU Community Initiative Interreg III A

Cross-border co-operation between the Free State of Saxony and the Republic of Poland
(Voivodship Lower Silesia)

Warsaw, 10.11.2006



Table of contents

1. Best practice which should be continued in the new programming period
2. Problems in managing the programm
3. Possibilities of simplifications within the managing system
4. N+2 risk and measures taken to avoid
5. Experience of co-operation with lead partners, the Lead Partner Principle in the future
6. „best- practice“ Interreg III A project examples
7. contact details

1. Best practice which should be continued in the new programming period

1.1 Polish staff located in the Joint Technical Secretariat

1.2 regular consultation days for both Saxon and Polish applicants

1.3 joint organisation of information events on both sides of the border

2. Problems in managing the programme

2.1 potential of the Saxon-Polish eligible area and infrastructure projects

2.2 late start of decisions about Polish projects in the steering committee


2.3 an automatic datatransfer is missing

2.4 difficulties concerning competence and responsibilities of programme actors



2.5 different legal framework conditions

2.6 national substructures and missing transparency in national project assessment

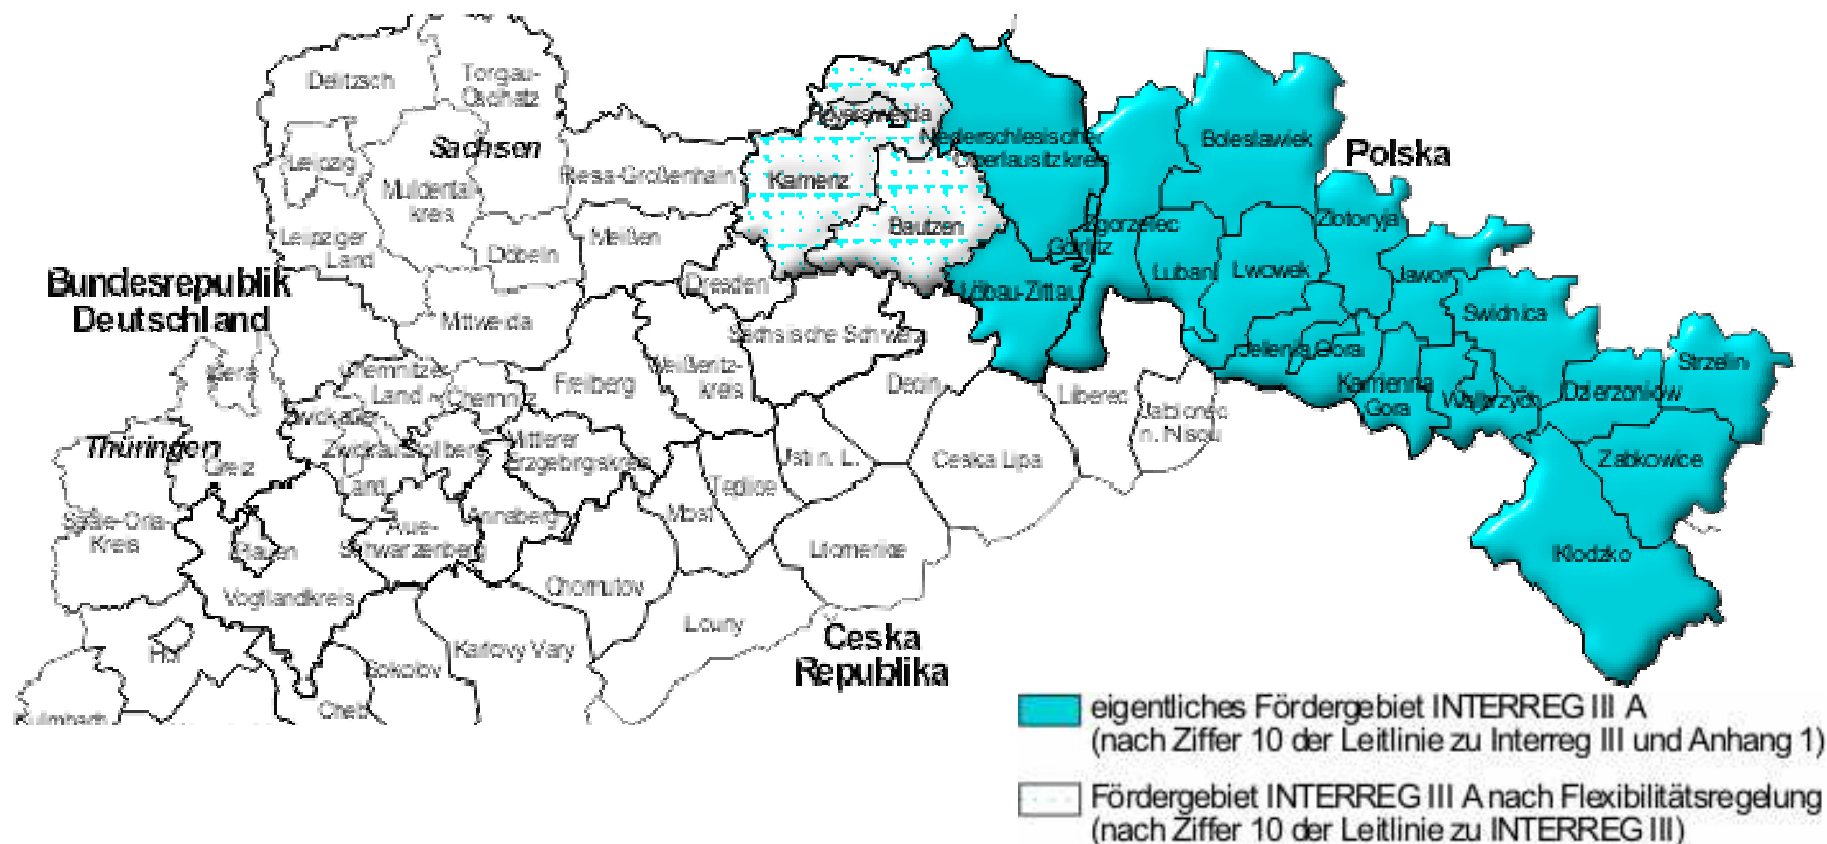2.1 Saxon-Polish eligible area 2004-2006



2.1 Saxon-Polish eligible area 2007-2013

-  obszar wsparcia projektów infrastrukturalnych
-  obszar wsparcia projektów "miękkich"



This project is co-financed
by the EUROPEAN UNION.




3. Possibilities of simplifications within the managing system


3.1 Interreg III A administration structures at programme level

3.1 Objective 3 administration structures at programme level

3.1 Interreg III A Administration structures at programme level

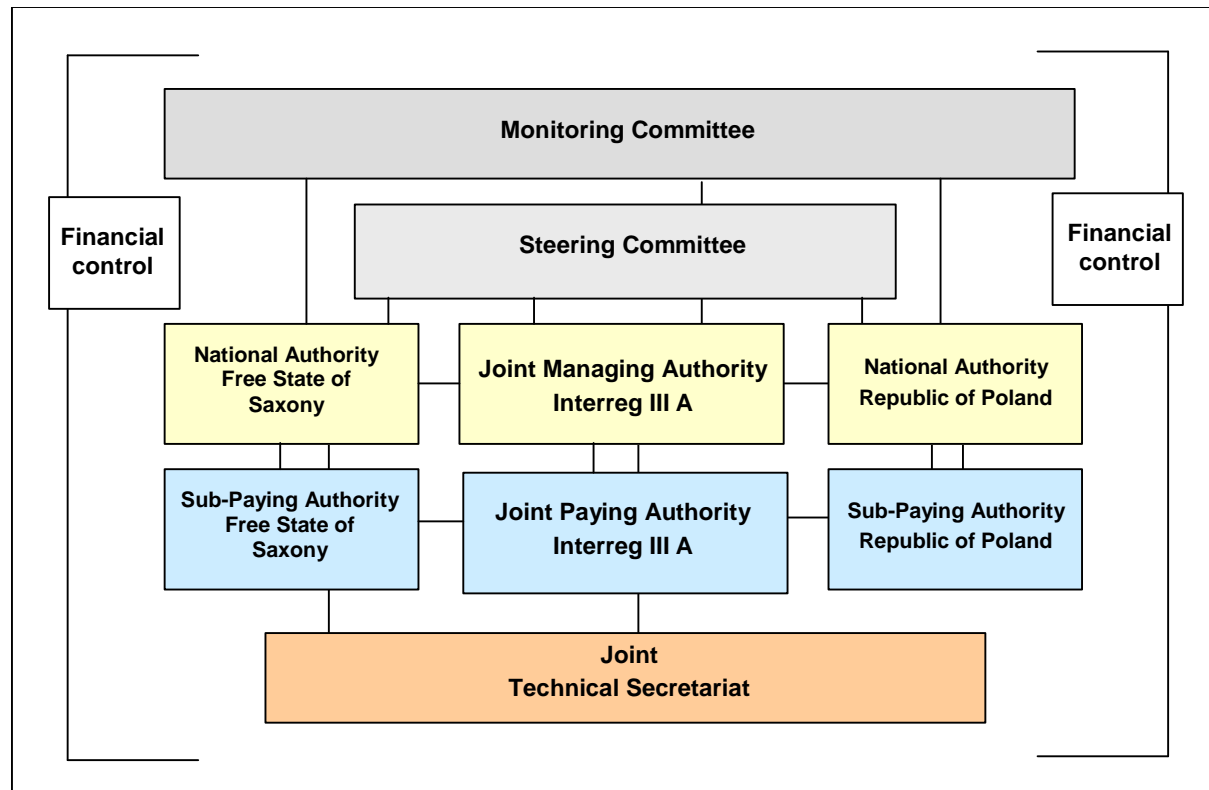

3.2 Objective 3 Administration structures at programme level

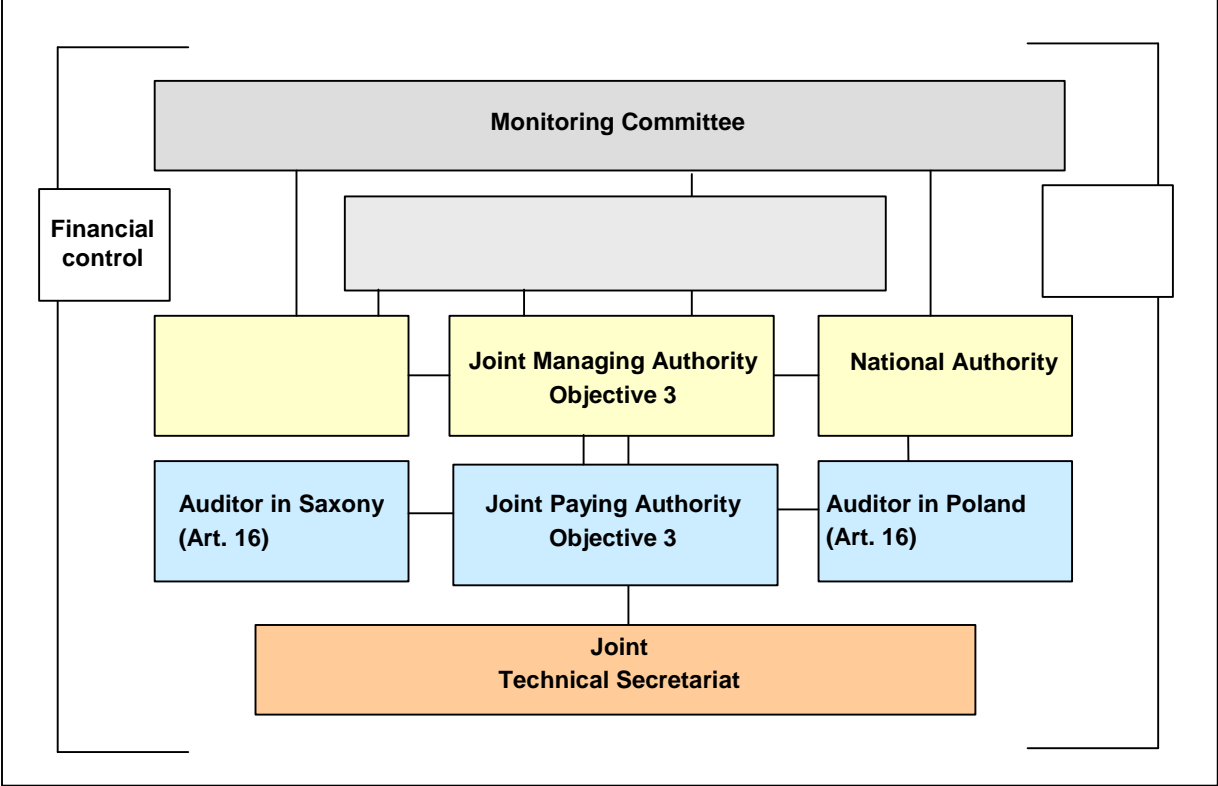

4. N+2 risk and measures taken to avoid

4.1 Financial budget and current allocation at programme level

4.2 N+2 risk 2007

4.3 measures taken to avoid

4.1 Financial budget and current allocation at programme level


Free State of Saxony

- Saxon-Lower Silesian border area: 45,03 Mio €
- > 95 % allocated per 09/06

Republic of Poland

(Voivodship Lower Silesia)

- Lower Silesian-Saxon border area: 26,61 Mio €
- > 95 % allocated per 09/06



4.2 N+2 risk 2007

Podstawa do obliczeń n+2	(€)
(Zaliczka+ Wykonanie do 2005 + Prognoza 2006)	29.019.258,49
7%-zaliczka dla Saksonii (2001)	3.083.150,02
Wydatki do 31.12.2005	15.873.780,95
Prognoza 2006	10.062.327,52
<i>w tym Wolny Kraj Związkowy Saksonia (wydatki do 31.12.2006)</i>	<i>8.565.500,00</i>
<i>w tym Rzeczpospolita Polska (wydatki do 31.07.2006)</i>	<i>1.496.827,52</i>
Różnica do wykonania reguły n+2	-4.704.590,19

4.2 N+2 risk 2007

Grundlage für Berechnung n+2	(€)
(Vorauszahl. + IST-AE bis 2005 + Vorausschätz. 2006)	29.019.258,49
7%-Vorschausszahl. für Sachsen (2001)	3.083.150,02
Ausgaben bis 31.12.2005	15.873.780,95
Vorausschätzung 2006	10.062.327,52
<i>davon Freistaat Sachsen (Ausgaben 31.12.2006)</i>	<i>8.565.500,00</i>
<i>davon Republik Polen (Ausgaben 31.07.2006)</i>	<i>1.496.827,52</i>
Differenz zu n+2-Erfüllung	-4.704.590,19

4.3 measures taken to avoid the N+2 risk

- project monitoring
 - supervising of project progress
 - supervising the payments and observing the rule N+2
- search new projects as compensation for projects which was cancelled
- using maximal financial interest (75 %) of European Union per project in 2007
- certification of expenditure without previous article 4 checks

5. Experience of co-operation with lead partners, the “LPP” in the future

5.1 Interreg III A types of projects

5.2 Interreg III A- co-operation platform

5.3 Interreg III A- project database

5.4 the “Lead Partner principle” in the future

5.1 Interreg III A types of projects

Simple Project

- implementation of the project in only one country, but with effects for the neighbour region

Mirror Project

- on both sides of the border a project is implemented, but there are nor direct organisational neither temporal connexions existing

Progressive Project

- on both sides of the border parts of the projects are implemented, both projects are connected by contents and organisational and temporal terms
(2 project applications, decision in the same SC meeting necessary)

5.2 Interreg III A- co-operation platform

The screenshot shows the Interreg III A website interface. At the top, there is a navigation menu with options like 'abgemeldet', 'Startseite', 'Einrichtungen / Firmen', 'Kooperationsdatenbank', 'FAQ', 'Kontakt', and 'Impressum'. Below this is a large banner with the text 'Kooperationsbörse' and the Interreg III A logo. The main content area is titled 'Liste der registrierten Einrichtungen / Unternehmen:' and contains a list of three entries. Each entry includes the name of the organization, a brief description, and the target group. On the left side, there is a sidebar with a 'LOGIN' section (E-Mail, Passwort, ANMELDEN) and a 'FILTER' section (Staat, Tätigkeitsfeld, Suchbegriff, SUCHE). The browser window title is 'Interreg III A - hallo nachbar | Einrichtungen / Firmen - Microsoft Internet Explorer provided by SAB'.

language selection is possible,
but no automatic translation

5.3 Interreg III A- Project database

Interreg III A - hallo nachbar | Projekte - Microsoft Internet Explorer provided by SAB

Adresse http://www.interreg3a.info/templates/tyTP_projects.php?topic=Projektdatenbank

LANGUAGES FAQ > SITEMAP > IMPRESSUM

Aktuelles
Förderungen
Antragspaket
Publikationen
Kooperationsbörse
Kontakte

STARTSEITE > AKTUELLES > PROJEKTE

Veranstaltungen
Termine
Newsletter
Pressemeldungen
Umsetzungsstand
Evaluierungen
Projekte

SUCHE

Interreg III A - Projektdatenbank

Für die beiden Interreg III A - Programme

- Freistaat Sachsen - Republik Polen (Woiwodschaft Niederschlesien) und
- Freistaat Sachsen - Tschechische Republik

finden Sie eine repräsentative Auswahl von Projekten, die seit 2001, d.h. nach Genehmigung der o.g. Programme durch die Europäische Kommission, gefördert wurden. Sie haben die Möglichkeit, Ihre Suche durch Setzen von Filtern bzw. Eingabe von Stichworten (Erweiterte Suche) zu spezifizieren. Die Projektdatenbank ist zurzeit nur in deutscher Sprache verfügbar und beinhaltet derzeitig nur sächsische grenzüberschreitende Vorhaben.

Die Projektdatenbank wird sukzessive in den kommenden Wochen und Monaten erweitert.

Projekt

Errichtung einer Pumpstation in Hagenwerder (2003) >>
Zweckverband Wasserversorgung Ostritz-Reichenbach

S 131 - Ausbau OD Rietschen (2004) >>
Straßenbauamt Bautzen

Deutsch - Polnische Wirtschaftstage 2004 - Bilaterale Unternehmensbegleitung (2004) >>
Entwicklungsgesellschaft Niederschlesische Oberlausitz GmbH

Telekardiologisches Netzwerk Ostachsen des Städtischen Klinikums Görlitz gmbH (2004) >>
Städtisches Klinikum Görlitz

S121 Fahrbahnerneuerung westlich Niesky, 1. Teilschnitt (2004) >>
Straßenbauamt Bautzen

Machbarkeitsstudie für den Aufbau von grenzüberschreitenden Produktions- und Vertriebskooperationen im Bekleidungs- und Schwerkonfektionsektor (2004) >>
Schwerkonfektionsektor (2004)

Filter

Programm: Alle
Priorität: Alle
Maßnahme: Alle
Projektträger: Alle
Landkreis: Alle
Euroregion: Alle

Filtern

Suche

Projekttitel:
Projektnummer:

Suchen

Erweiterte Suche

Suchbegriff:

Suchen

Vertrauenswürdige Sites

Start | Posteingang - Micr... | Microsoft Word | Interreg III A - ... | Microsoft PowerPoi... | 13:58

A project database for Saxon and Polish projects in the language of the beneficiary

5.4 the “Lead Partner principle” in the future

Challenges to be faced in the New Programming Period:

- Joint development
- Joint implementation
- Joint staffing
- Joint financing

Project generation will be the basis for successful programme implementation. The applicants will need more support than for the development of an Interreg III A project.

6. „best- practice“ Interreg III A project examples

6.1 project example „Transport Infrastructure“

6.2 project example „Transport Infrastructure“

6.1 project example „Transport Infrastructure“


<u>Project title:</u>	Construction of the traffic facility of border crossing Hagenwerder – Radmerice (PL)
<u>Beneficiary:</u>	Road Construction Office Bautzen
<u>Project duration:</u>	04.10.2001 – 30.10.2006
<u>Total costs:</u>	4,02 Mio. €
<u>EU budget:</u>	2,41 Mio. €
<u>Contents:</u>	<ul style="list-style-type: none">● Reconstruction of Neiße crossing between Hagenwerder and Radmerice● New building of state road S 128 between the German federal road B 99 and the Polish Voivodship road No. 357; 172 m long Neiße bridge and 128 m long flood bridge
<u>Cross-border effects:</u>	<ul style="list-style-type: none">● Phare CBC project in Poland● Bridging the gap for cross-border traffic connexion



This project is co-financed
by the EUROPEAN UNION.



Construction of the traffic facility of border crossing Hagenwerder – Radmerice (PL)

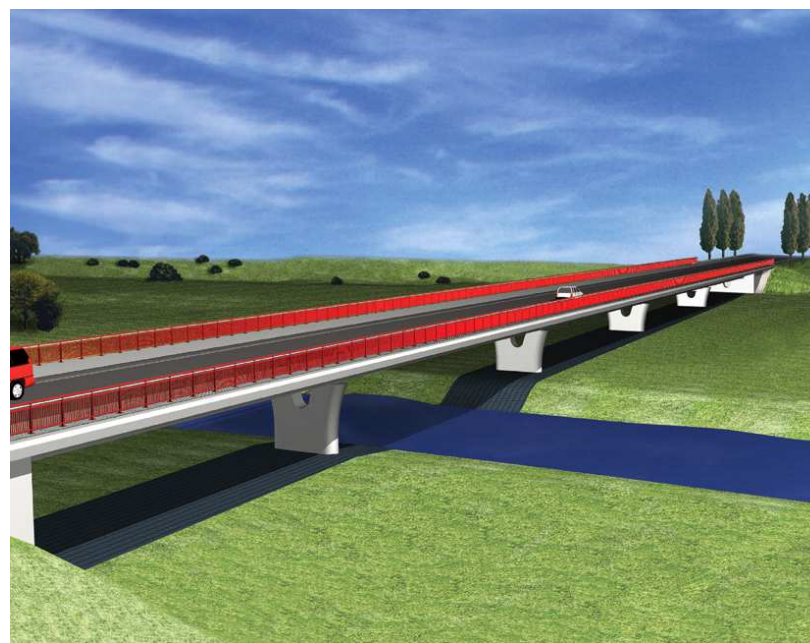

This project is co-financed
by the EUROPEAN UNION.



Seite 22

6.2 project example „Transport Infrastructure“

<u>Project title:</u>	Old Town Bridge Görlitz
<u>Beneficiary:</u>	City of Görlitz
<u>Project duration:</u>	11/2002 – 12/2004
<u>Total costs:</u>	3,1 Mio €
<u>EU budget:</u>	1,15 Mio €
<u>Content:</u>	<ul style="list-style-type: none">● Reconstruction of the Old Town Bridge over the Neiße river for pedestrians and cyclists (one carriageway and two footpaths)● Length 82.5 m and width 4.50 m
<u>Cross-border effects:</u>	<ul style="list-style-type: none">● Further the development of economic and cultural exchange● First joint construction of the European city Görlitz/Zgorzelec

Old Town Bridge Görlitz



This project is co-financed
by the EUROPEAN UNION.



Seite 24

7. Contact details

Address: Sächsische Aufbaubank – Förderbank -
Gemeinsames Technisches Sekretariat
Pirnaische Straße 9
01069 Dresden

Phone: 0049 (0351) 4910 – 1860

Fax: 0049 (0351) 4910 – 1870

E-mail: kontakt@interreg3a.info

Homepage: www.interreg3a.info
www.sab.sachsen.de

7. Contact details

Address: Sächsisches Staatsministerium für Wirtschaft und Arbeit
Referat 36
Gemeinsame Verwaltungsbehörde Interreg III A
Wilhelm- Buck- Str. 2
01097 Dresden

Phone: 0049 (0351) 564 – 8363

Fax: 0049 (0351) 564 – 8306

E-mail: brigitte.czanik@smwa.sachsen.de

Homepage: www.interreg3a.info
www.sab.sachsen.de
